PAMPANGA STATE AGRICULTURAL UNIVERSITY
Project Monitoring Committee

PSAU
Document Control#: 354

August 20, 2025

PAMPANGA STATE AGRICULTURAL UNIVERSITY
MAGALANG, PAMPANGA
RECEIVED
DATE: 8-28-25 TIME: 2:06
BY:
RECORDS UNIT 1904

DR. ANITA G. DAVID
SUC President IV
This University

Subject: **Request for Approval of 2nd Time Extension for DAPER Construction & Trading**

Dear Madam President,

I hope this letter finds you in good health and high spirits.

This letter serves as an official endorsement of the request submitted by DAPER Construction and Trading for a time extension on the project entitled Construction of Animal Science and Fisheries Building.

The contractor has presented sufficient documentation, including reports that circulated on the suspension of work in government agencies, substantiating the occurrence of multiple typhoons within the project timeline. These extreme weather events have resulted in the issuance of work suspension orders from various government agencies, directly impacting project progress and operational safety. During the construction process, several on-site issues were identified, deliberated, and resolved. These matters were subsequently endorsed by the PMC to the Technical Working Group – Infrastructure, in coordination with the University Engineer, for review as part of the Variation Order. The contractor has also incorporated these issues into their formal request.

After thorough evaluation of the submitted documents and in consideration of the disruptions caused by the inclement weather conditions and the resolving the issues on Variation Order, our office finds the justification both valid and compelling. In line with existing policies and in the interest of fair project implementation, we hereby endorse the contractor's request for a time extension of **27 days** (9 days for the inclement weather and 18 days for the coordination meetings and review of the proposed variation order), subject to applicable provisions and continued monitoring. (*Please see attachments*).

We trust that this endorsement will assist in facilitating the necessary procedural adjustments and ensure the successful completion of the aforementioned project.

Thank you for your usual support.

Yours sincerely,

MARIA CRISELLA DC. MERCADO, DTech, LPT
PMC Head

DR. RODEL T. LORENZO
PMC Member

DR. SOLOMON L. ROQUE
PMC Member

ENGR. RONNIE E. BRIONES
PMC Member

ENGR. PAULO JAY B. RIVERA
PMC Member

MS. MARIE ANNE D. VALERIO
PMC Member

MR. ROGELIO G. ISIP
PMC Member

ATTY. REYMON E. FABROS
PMC Member

Recommending Approval:

MS. MINA LYN G. ALVIZ, MAED
Vice President – Admin. and Finance
Actg

APPROVED:

ANITA G. DAVID, EdD
University President

PSAU PRESIDENT'S OFFICE
RECEIVED
p. 144
8/29
DATE
MAGALANG PAMPANGA

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING GENERAL BUILDING
246 San Nicolas City of San Fernando, Pamp.2000
09982593644
Email:cndavid06@yahoo.com
09065480445

18 August 2025

Dr. Maria Crisella DC. Mercado
Head, Project Monitoring Committee
Pampanga State Agricultural University
Magalang, Pampanga

Subject: Request for Time Extension Due to Work Suspension from Inclement Weather and School Power Maintenance and Variation Orders

Dear **Dr. Mercado,**

Warmest greetings.

We respectfully write to request an extension of contract time for the ongoing construction project due to unavoidable work suspensions and the approved variation orders for structural works.

On 18 July 2025, construction activities were suspended following a school-wide announcement of a work stoppage for all employees in relation to scheduled electrical maintenance. This rendered the site inaccessible and unsafe for continued operations.

In addition, continuous inclement weather conditions from 19 July to 26 July 2025 forced the suspension of site works. The heavy rains and unsafe ground conditions during this period made it impractical and hazardous to proceed with construction activities.

Furthermore, we respectfully invoke the provisions of **Republic Act 9184, Annex "E" of its Implementing Rules and Regulations (Contract Implementation Guidelines)**, which provide that:

- **Item 1(c):** *"The extension of contract time is allowed due to the implementation of extra work orders or change orders due to… variations, provided that such work is within the general scope of the project as bid and awarded."*
- **Item 2:** *"Extension of contract time shall be granted when the work is increased in scope… and equivalent additional time shall be allowed."*

As the approved variation orders for structural works amount to ten percent (10%) of the original contract cost, a corresponding extension equivalent to ten percent (10%) of the original 180 calendar days, or **eighteen (18) calendar days**, is justifiable.

In light of the above, we are formally requesting a total extension of **twenty-seven (27) calendar days**—comprising nine (9) calendar days due to force majeure events (school-mandated suspension and inclement weather) and eighteen (18) calendar days corresponding to the approved variation orders.

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING **GENERAL BUILDING**
246 San Nicolas City of San Fernando, Pamp.2000 Email:cndavid06@yahoo.com
09982593644 09065480445

We assure you that every effort continues to be made to maintain progress and mitigate delays. We remain committed to the timely and quality completion of the project. We hope for your kind understanding and favorable consideration of this request. Should you require any supporting documentation such as weather bulletins, internal logs, or variation order approvals, we are ready to provide them.

Respectfully yours,

Thank you very much.

Respectfully yours,

ENGR. JAN VINCENT A. SACRAMENTO
Project-in-Charge
Daper Construction and Trading

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING GENERAL BUILDING
246 San Nicolas City of San Fernando, Pamp.2000
09982593644
Email:cndavid06@yahoo.com
09065480445

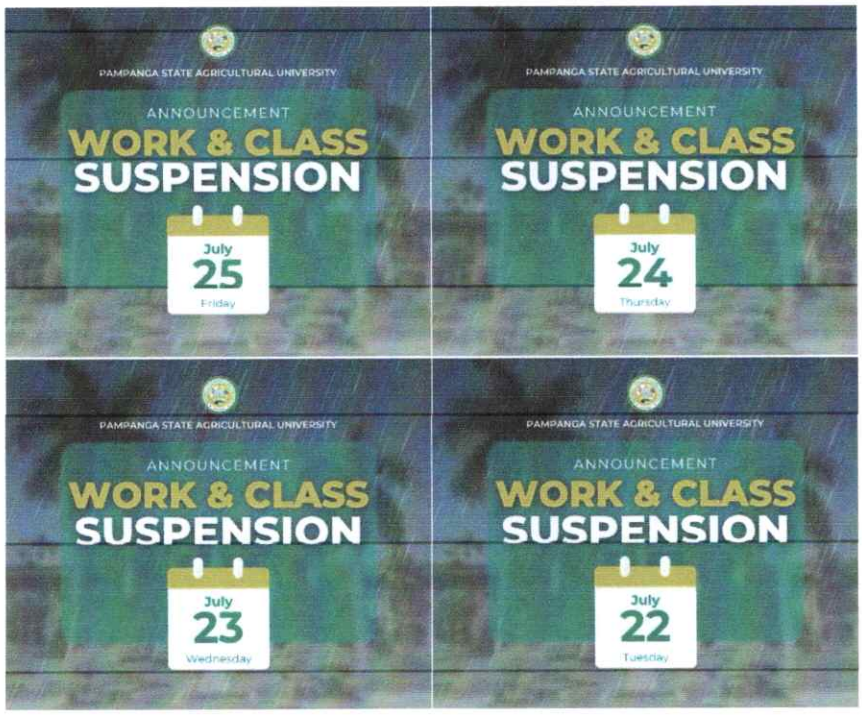

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING GENERAL BUILDING
246 San Nicolas City of San Fernando, Pamp.2000
09982593644
Email:cndavid06@yahoo.com
09065480445

13	14	15	16	17	18	19
32°	33°	32°	33°	31°	28°	27°
24°	24°	24°	24°	24°	23°	23°

20	21	22	23	24	25	26
30°	27°	27°	27°	26°	30°	30°
24°	23°	23°	24°	24°	24°	25°

Day
27°

Night
23°

Record High
34°

Average High
31°

Record Low
22°

Average Low
24°

Sunrise
5:37 am

Sunset
6:31 pm

Moonrise
1:38 am

Moonset
3:13 pm

Waning Crescent

Republic of the Philippines
PAMPANGA STATE AGRICULTURAL UNIVERSITY
TECHNICAL WORKING GROUP

PAMPANGA STATE AGRICULTURAL UNIVERSITY
MAGALANG, PAMPANGA
RECEIVED
DATE: 8/20/25 TIME: 3:25
BY:
RECORDS UNIT

August 20, 2025

PSAU
Document Control#: 331

ANITA G. DAVID, Ed.D.
SUC President IV
This University

THRU: DR. LYNDON SOLIS
BAC Chairman / VP for Planning and Resource Generation

Subject: **Request to approve Variation Order for the project Construction of Animal Science and Fisheries Building**

Dear Dr. David,

This is in reference to the letter endorsed by the Project Monitoring Committee (PMC), originally submitted by DAPER Construction and Trading dated June 26, 2025, and received by our office on July 2, 2025. The letter requests the approval of the Variation Order due to additional concrete and concrete hollow blocks required for the construction project.

The request complies with the provisions of Republic Act 9184 and its Revised Implementing Rules and Regulations, Annex E, which allow for variation orders when actual field conditions necessitate changes in the original contract.

DAPER Construction cited that the increase in quantities was necessary to address site conditions that were not reasonably foreseen during the preparation of the Bill of Quantities. These additions are essential to ensure the satisfactory completion of the project.

The total cost implication submitted by the contractor amounts to **P1,486,270.06**. After a thorough evaluation and computation by the Technical Working Group (TWG) and witnessed by PMC, it was determined that a variation order is justified. However, based on our assessment, the approved amount for the variation order is **P620,742.95**.

Attached for your reference is the detailed computation and justification for the proposed variation.

We respectfully seek your review and approval of the attached variation order.

Best regards,

Ronnie E. Briones
TWG- Head

T.O from 8/18 – 8/20

Engr. Rosemarie S. Macmac
TWG - Member

Dr. Anthony C. Nicdao
TWG -Member

Engr. Praulyne S. Rivera
TWG - Member

TWG No. 2025-005

Pampanga State Agricultural University
PROJECT MONITORING COMMITTEE

PAMPANGA STATE AGRICULTURAL UNIVERSITY
MAGALANG, PAMPANGA
RECEIVED
DATE: 7/1/26 TIME: 1:24
BY: 1498
RECORDS UNIT

June 30, 2025

ENGR. RONNIE E. BRIONES
Chair,
Technical Working Group - Infrastructure
This University

Subject: **Endorsement for the Review of the Bill of Quantities for the Variation Order Request from DAPER Construction and Trading**

Dear Engr. Briones,

We respectfully forward for your consideration our recommendation regarding the variation order request submitted by DAPER Construction and Trading.

The contractor has formally requested a meeting with the designer, as well as representatives from the PMC and TWG, to deliberate on the matter and formulate the attached proposal.

In light of these circumstances, the PMC strongly recommends prompt action to prevent further delays in the project's implementation.

Accordingly, we endorse the contractor's request, including the proposed costing of the affected building components, and respectfully seek your endorsement to the University President upon completion of your review and necessary revisions.

Thank you for your continued support.

Sincerely yours,

DR. MARIA CRISELLA DC. MERCADO
Project Monitoring Committee Head

DR. RODEL T. LORENZO
PMC Member

DR. SOLOMON L. ROQUE
PMC Member

ENGR. PAULO JAY B. RIVERA
PMC Member

ENGR. RONNIE E. BRIONES
PMC Member

MS. MARIE ANNE D. VALERIO
PMC Member

MR. ROGELIO G. ISIP
PMC Member

ATTY. REYMON E. FABROS
Legal Officer IV / PMC Member

Noted:

MR. KEVIN AARON PERALTA
Project Development Officer III

DR. RAFAEL R. RAFAEL
Director for Planning and Development

MS. MINA LYN G. ALVIZ, MAED
Acting Vice President for Administration and Finance

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING **GENERAL BUILDING**

26 June 2025

Dr. Maria Crisella DC. Mercado
Head, Project Monitoring Committee
Pampanga State Agricultural University
Magalang, Pampanga

Subject: Proposal for Revision of Initial Structural Roof Framing Design

Dear Dr. Kreez,

Greetings.
We extend our sincere appreciation for your continued support and collaboration on the **Construction of Animal and Fisheries Building.**
Following our detailed evaluation of the initial structural roof framing design and subsequent coordination with our construction team, we respectfully propose a revision to the current roof framing layout. This recommendation stems from the need to enhance **constructibility and overall viability** of the structural system while maintaining full compliance with the **National Structural Code of the Philippines (NSCP) 2015**.

The key considerations for our proposed revision are as follows:

1. **Improved Constructibility**
   The revised framing design simplifies site implementation, accounting for actual field conditions and available construction equipment. It promotes safer and more efficient erection of structural elements, thereby reducing construction time and minimizing potential delays.
2. **Structural Viability and Optimization**
   The proposed layout enhances structural behavior by optimizing load paths and minimizing deflection and stress concentrations. Member sizing and spacing have been rationalized to achieve a balance between strength, stiffness, and material economy.
3. **Code Compliance**
   All proposed revisions were developed in strict accordance with **NSCP 2015**, particularly the provisions for steel structures, live and environmental loads, and connection design. The integrity and safety of the structure remain the utmost priority.

In support of this proposal, we are submitting the revised structural roof framing plans, along with preliminary analysis and relevant details for your technical review. We believe that these revisions are not only feasible but offer tangible benefits to the execution and durability of the project.

We respectfully request the endorsement of the Technical Working Group to adopt the proposed revisions as part of the approved structural documentation. We are prepared to present and discuss the details further at your convenience, and we remain committed to upholding the project's structural integrity, cost-efficiency, and schedule performance.
Thank you for your attention and continued support.

Respectfully yours,

Engr. Jan Vincent A. Sacramento, M.Eng. S.E.
Daper Construction and Trading

cc:TWG

PAMPANGA STATE AGRICULTURAL UNIVERSITY
Office of the President

ACTION SLIP

DATE: 8/19/2025

TO: Dr. MCDC Mercado

(✓) For URGENT action, please
( ) For your action, please
( ) For information, please
( ) For submission/compliance, please
( ) For endorsement, please
( ) For dissemination, please
( ) For recommendation, please
( ) For coordination, please
( ) For your participation, please
( ) For your initial/signature, please
( ) Please take up with me.
( ) Please set a Meeting.
( ) Please draft Office Order/s.
( ) Please draft Letter/s.
( ) Please see correction/s.
( ) Please file.

Thank you,

ANITA G. DAVID, Ed. D.
University President

PSAU-OPR-SF-03 | 03 (04-01-24)

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING GENERAL BUILDING
246 San Nicolas City of San Fernando, Pamp.2000
09982593644
Email:cndavid06@yahoo.com
09065480445

18 August 2025

PAMPANGA STATE AGRICULTURAL UNIVERSITY
MAGALANG, PAMPANGA
RECEIVED
DATE: 8-18-25 TIME: 3:37
BY:
RECORDS UNIT 2628

DR. ANITA G. DAVID
President
Pampanga State Agricultural University
Magalang, Pampanga

Subject: Soft Follow up for Variation Order Resolution

Dear **Pres. David,**
Warmest greetings.

We respectfully write to follow up on our official communication dated **June 26, 2025**, regarding the request for approval of variation orders for the ongoing construction project. As provided under **Republic Act No. 9184 and its Implementing Rules and Regulations (IRR), Annex "E" (Contract Implementation Guidelines), Section 3**, variation orders shall be processed and acted upon within a period of thirty (30) calendar days from official submission.

As of this date, more than thirty (30) calendar days have lapsed since our submission, and we have yet to receive the final resolution on the matter. We fully understand that such requests undergo a thorough review process, and we sincerely appreciate the diligence of your office in safeguarding compliance with procurement laws and ensuring the proper execution of the project.

However, we respectfully bring to your attention that the requested variation orders form part of the **critical path** for the completion of the project. Without their timely approval, the implementation of essential works will be hampered, directly affecting the project's finality. Should this remain unresolved, we may be reluctantly compelled to invoke our contractual rights under **Annex "E", Item 4 of the IRR of RA 9184**, which states:

"The contractor may suspend work operations on any or all projects/activities upon receipt of an order of the procuring entity or for causes beyond the control of the contractor such as... non-approval of requested variation orders."

In this regard, and in the spirit of maintaining progress without interruption, we respectfully request that the resolution of the pending variation orders be issued within **seven (7) calendar days** from receipt of this letter. This will enable us to proceed with the works seamlessly and ensure the project's timely delivery.

We assure you that our foremost objective is to avoid any disruption and to continue the project smoothly in close coordination with your office. We remain ready to provide any additional documentation or clarification that may be required to facilitate the resolution.

Thank you very much for your kind understanding and immediate consideration.

Respectfully yours,

PSAU PRESIDENT'S OFFICE
RECEIVED
P.100
8/19
DATE
MAGALANG PAMPANGA

8-20-25 3:26

DAPER CONSTRUCTION AND TRADING
GENERAL ENGINEERING **GENERAL BUILDING**
246 San Nicolas City of San Fernando, Pamp 2000
09982593644
Email:cndavid06@yahoo.com
09065480445

ENGR. JAN VINCENT A. SACRAMENTO
Project-in-Charge
Daper Construction and Trading

Cc:

PMC

TWG

PSAU PRESIDENT'S OFFICE
RECEIVED
p.100
8/19
DATE
MAGALANG PAMPANGA

PAMPANGA STATE AGRICULTURAL UNIVERSITY
Office of the President

August 22, 2025

AR. CANDIDO DAVID
Proprietor
DAPER Construction and Trading
Kristina St. cor. Ruperta St.
Lourdes Heights Subd. Del Rosario,
City of San Fernando, Pampanga

Subject: **Approval of 2nd Time Extension Request – *Construction of Animal Science* Building**

Dear Ar. David],

This letter serves as formal approval of your request for a time extension of **twenty-seven (27)** calendar days for the completion of the Construction of the Animal Science Building.

Following the endorsement of the Project Monitoring Committee (PMC) and in coordination with the Technical Working Group – Infrastructure and the University Engineer, your request has been thoroughly reviewed. The extension is granted in consideration of the inclement weather and on-site issues encountered during the construction phase, which were discussed and resolved collaboratively. These issues have been evaluated and included as part of the Variation Order submitted.

Accordingly, the revised completion date for the project shall be adjusted to **October 9, 2025**, based on the approved extension period. Please ensure that all necessary adjustments to your project timeline and deliverables are reflected accordingly.

We trust that this extension will support the successful and timely completion of the project. Should you have further concerns or require clarification, please do not hesitate to coordinate with the University Engineer or the PMC.

Thank you for your continued commitment to quality and collaboration.

Sincerely,

ANITA G. DAVID, EdD
SUC President IV
