**PAMPANGA STATE AGRICULTURAL UNIVERSITY**
**Project Monitoring Committee**

**PSAU**
**Document Control#: 353**

August 27, 2025

PAMPANGA STATE AGRICULTURAL UNIVERSITY
MAGALANG, PAMPANGA
RECEIVED
DATE: 8.28.25 TIME: 2:07
BY:
RECORDS UNIT 1905

**DR. ANITA G. DAVID**
SUC President IV
This University

Subject: **Request for Approval of 1st Time Extension for KATS Construction & Trading**

Dear Madam President,

I hope this letter finds you in good health and high spirits.

This letter serves as an official endorsement of the request submitted by KATS Construction and Trading for a time extension on the project entitled Repair and Rehabilitation of the Farmer's Training Center.

The contractor has presented sufficient documentation, including reports that circulated on the suspension of work in government agencies, substantiating the occurrence of multiple typhoons within the project timeline. These extreme weather events have resulted in the issuance of work suspension orders from various government agencies, directly impacting project progress and operational safety. During the construction process, several on-site issues were identified, deliberated, and resolved. The contractor has also incorporated these issues into their formal request.

After thorough evaluation of the submitted documents and in consideration of the disruptions caused by the inclement weather conditions and some on-site conditions, our office finds the justification both valid and compelling. In line with existing policies and in the interest of fair project implementation, we hereby endorse the contractor's request for a time extension of **17 days** (9 days for the inclement weather and 8 days for the coordination meetings and review of the on-site issues and concerns), subject to applicable provisions and continued monitoring. (*Please see attachments*).

We trust that this endorsement will assist in facilitating the necessary procedural adjustments and ensure the successful completion of the aforementioned project.

Thank you for your usual support.

Yours sincerely,

**MARIA CRISELLA DC. MERCADO, DTech, LPT**
PMC Head

**DR. RODEL T. LORENZO**
PMC Member

**DR. SOLOMON L. ROQUE**
PMC Member

**ENGR. RONNIE E. BRIONES**
PMC Member

**ENGR. PAULO JAY B. RIVERA**
PMC Member

**MS. MARIE ANNE D. VALERIO**
PMC Member

**MR. ROGELIO G. ISIP**
PMC Member

**ATTY. REYMON E. FABROS**
PMC Member

Recommending Approval:

**MS. MINA LYN G. ALVIZ, MAED**
Acting Vice President – Admin. and Finance

APPROVED:

**ANITA G. DAVID, EdD**
University President

PSAU PRESIDENT'S OFFICE
RECEIVED
p.199
8/29
DATE
MAGALANG, PAMPANGA

K.A.T.S. CONSTRUCTION & TRADING
19 San Nicolas 1, Magalang, Pampanga 2011
Cel. No. 0922-835-5732 E-mail : yaj8569@gmail.com

August 14, 2025

**Dr. Anita G. David**
University President
Pampanga State Agricultural University

**Thru: Dr. Maria Crisella DC. Mercado**
Head of Project Monitoring Committee

**Subject: Request for Time Extension for Repair and Rehabilitation of Farmers' Training Center**

Dear Madam,

We refer to the above-mentioned project and hereby submit a request for a time extension for the completion of the **Repair and Rehabilitation of Farmers' Training Center.** The original completion date for this project is September 13, 2025, and we are requesting an adjusted completion date of October 13, 2025, a total of thirty (30) days to meet the completion of the remaining activities for the project.

The reason for this request is unexpected weather conditions, unforeseen site conditions, and changes with some of the design on the project.

During the past days, the effect of the monsoon weather affected our work activities. Fire safety compliance of the FTC building which was recently notified by the local Fire Department, unforeseen extended defects/damages on plumbing, tiles, electrical components to the FTC building, some design and scope of work changes, which led us to a certain number of days of delay.

We commit to fully completing the project with efficiency and coordinating with PSAU project in charge. We are confident that with this time extension, we can successfully complete the project.

We hope that our request will be given favorable consideration.

Respectfully yours,

**Romeo C. Supan, Jr.**
Proprietor
K.A.T.S. Construction and Trading

Headlines

**Monsoon rains to hammer Metro Manila, Luzon until Thursday**

Cristina Chi - Philstar.com

July 22, 2025 | 6:48am

ADVERTISEMENT

MANILA, Philippines — The southwest monsoon (habagat) is set to continue bringing heavy to moderate rainfall across Metro Manila, parts of Luzon, and portions of Visayas over the next three days, according to state weather bureau PAGASA's advisory early Tuesday morning, July 22.

In its 5 a.m. weather advisory, PAGASA warned of significant rainfall through Thursday, July 24.

**Rainfall outlook through Thursday.** On Tuesday, July 22, Metro Manila, Zambales, Bataan, Pampanga, Bulacan, Cavite, Batangas, Rizal and Occidental Mindoro are forecast to receive 100 to 200 millimeters of rain. Meanwhile, Pangasinan, Tarlac, Laguna, and Quezon can expect 50 to 100 millimeters.

The heavy downpour is predicted to continue on Wednesday, July 23, with 100 to 200 millimeters of rainfall anticipated in Metro Manila, Zambales, Bataan, Pampanga, Bulacan, Cavite, Batangas, Laguna, Rizal, and Occidental Mindoro.

Areas including Ilocos Norte, Ilocos Sur, La Union, Pangasinan, Tarlac, Quezon, Oriental Mindoro, Marinduque, Romblon, Masbate, Sorsogon, Albay, Camarines Sur, Catanduanes, Antique, Aklan, Capiz, Iloilo, Guimaras and Negros Occidental are expected to receive 50 to 100 millimeters of rainfall.

By Thursday, July 24, the monsoon will continue to affect parts of Northern and Central Luzon and Occidental Mindoro, with 100 to 200 millimeters of rain forecast for Ilocos Norte, Ilocos Sur, La Union, Pangasinan, Abra, Benguet, Zambales, Bataan and Occidental Mindoro.

Meanwhile, Metro Manila, Apayao, Tarlac, Pampanga, Bulacan, Cavite, Batangas, Rizal, Laguna, Quezon, Oriental Mindoro, Marinduque, Romblon, Masbate, Sorsogon, Albay, Camarines Sur, Aklan, and Antique may experience 50 to 100 millimeters of rain.

PAGASA noted that rainfall could be higher in mountainous and elevated areas, and previous rainfall might worsen the impact in some locations. Residents in affected areas should prepare for potential flooding and landslides.

**Two LPAs.** Alongside the monsoon, PAGASA weather specialist Obet Adrina noted in his 5 a.m. forecast that one of two low-pressure areas currently being monitored by PAGASA may develop into a tropical cyclone.

One LPA was last spotted at 3 a.m. east of Cagayan, while the other was seen east of Central Luzon.

"Depending on the development of the low-pressure area, the effect of the southwest monsoon may continue affecting most of Luzon and Visayas," Badrina said, adding that Mindanao is expected to see isolated thunderstorms.

"If either of the two LPAs develops into a tropical cyclone, it's unlikely to make landfall because its movement is northward," the PAGASA weather specialist added.

**Weather advisories vs heavy rainfall warnings.** PAGASA's weather advisories cover a 24-hour time frame and are issued at the provincial level to provide general guidance on potential weather disturbances.

In contrast, a heavy rainfall warning offers short-term forecasts that are valid for the next two to three hours.

These warnings are issued at the municipal level and utilize Doppler radar to monitor real-time rainfall intensity. Class suspensions, according to PAGASA, must be based on the heavy rainfall warnings issued by PAGASA regional services divisions.

Manila Standard

Last updated July 6, 2025, 10:18 AM

**NDRRMC: Habagat, Bising affect 13K people**

By Rex Espiritu

July 6, 2025, 9:58 AM

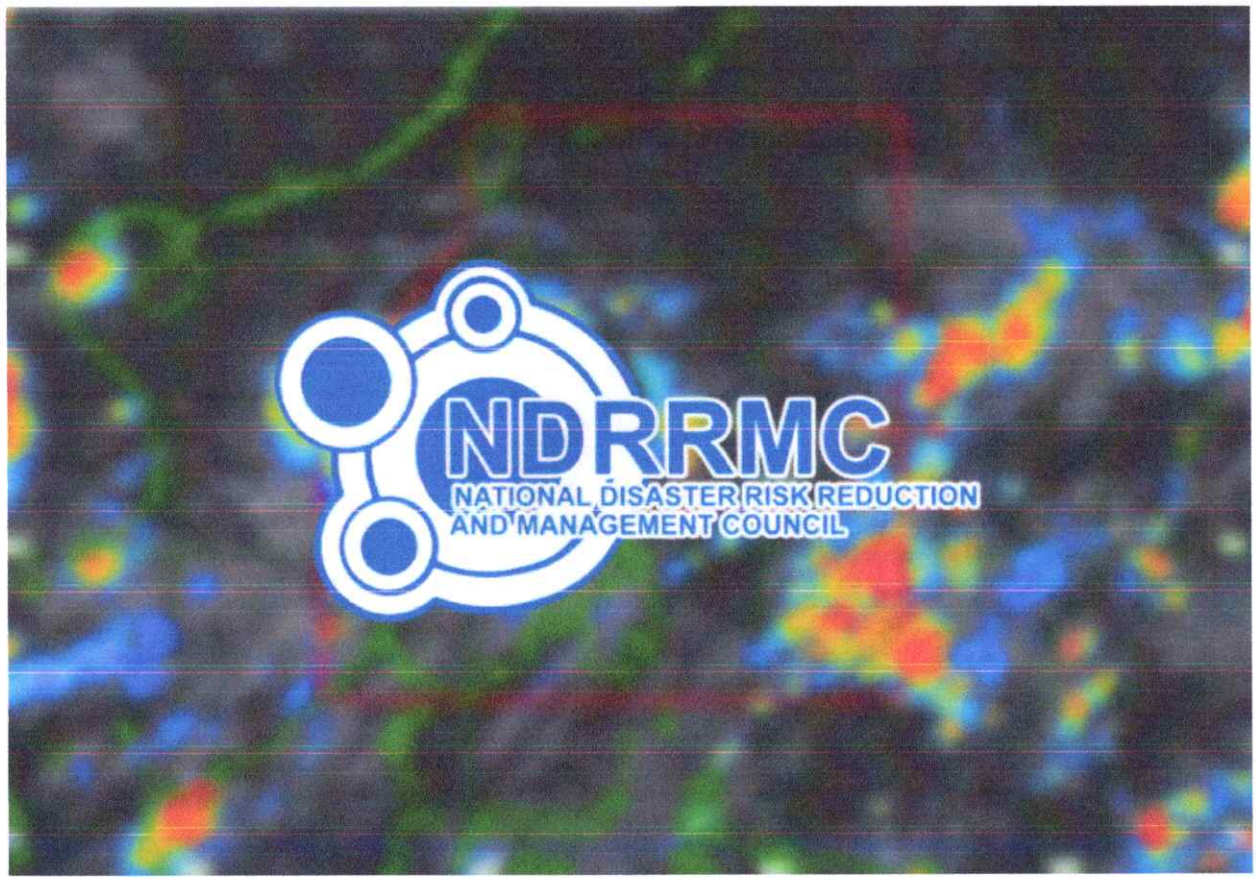


The combined effects of rains induced by the southwest monsoon (habagat) and storm 'Bising' affected over 13,000 individuals, the National Disaster Risk Reduction and Management Council (NDRRMC) said Sunday.

According to the disaster agency, these are equivalent to 3,773 families across 3 regions in the country. Central Luzon was hit hardest with 12,039 individuals affected or 3,413 families.

- Advertisement -

In the same region, 23 areas are still submerged with flood waters, especially in some cities and municipalities in Nueva Ecija, Pampanga, and Zambales.

The Lubuagan–Batong Buhay–Abra boundary road in Kalinga has been declared impassable following a soil and rock collapse that cut off access to Kadamayan Falls, a well-known tourist destination.

**#WalangPasok: Classes, gov't work suspended on Tuesday, July 22**

**By: Luisa Cabato, Zacarian Sarao - @inquirerdotnet**

INQUIRER.net / 05:02 PM July 21, 2025

Share:

Classes and government work are suspended on Tuesday, July 22, in some areas due to inclement weather. INQUIRER stock image

*[Updated July 21, 2025, 6:45 p.m.]*

MANILA, Philippines — All classes and government work are suspended on Tuesday, July 22, in Metro Manila and 10 other provinces, said the Department of the Interior and Local Government (DILG).

*Article continues after this advertisement*

**READ: LIVE UPDATES: Southwest monsoon weather continues after Crising leaves**

ADVERTISING

This followed Malacañang's approval of the suspension, as recommended by the Office of Civil Defense, Presidential Communications Office Secretary Dave Gomez told reporters on Monday.

According to the DILG, classes and government work are suspended on the following based on the recommendations of the Office of the Civil Defense and the Cabinet:

by Taboola

Sponsored Links

**You May Like**

**Play Trusted Games and Win [Sign Up]**Looking for a way to win real cash? Try our WinZir, licensed by PAGCOR. Start playing today.**WinZir**

- Metro Manila

- Zambales
- Bataan
- Pampanga
- Bulacan
- Cavite
- Batangas
- Rizal
- Pangasinan
- Tarlac
- Occidental Mindoro

FTC Common CR on Ground Floor

FTC Common CR on Ground Floor

FTC Common CR on Ground Floor

Lecture room Comfort Room

FTC Entrance Door

**PAMPANGA STATE AGRICULTURAL UNIVERSITY**
**Office of the President**

August 27, 2025

**ENGR. ROMEO SUPAN JR.**
Proprietor
KATS Construction and Trading
19 San Nicolas 1, Magalang, Pampanga

Subject: **Approval of 1nd Time Extension Request – Repair and Rehabilitation of the Farmer's Training Center**

Dear Engr. Supan,

This letter serves as formal approval of your request for a time extension of **seventeen (17)** calendar days for the completion of the Repair and Rehabilitation of the Farmer's Training Center.

Following the endorsement of the Project Monitoring Committee (PMC), your request has been thoroughly reviewed. The extension is granted in consideration of the inclement weather and on-site issues encountered during the construction phase, which were discussed and resolved collaboratively.

Accordingly, the revised completion date for the project shall be adjusted to **September 30, 2025**, based on the approved extension period. Please ensure that all necessary adjustments to your project timeline and deliverables are reflected accordingly.

We trust that this extension will support the successful and timely completion of the project. Should you have further concerns or require clarification, please do not hesitate to coordinate with the University Engineer or the PMC.

Thank you for your continued commitment to quality and collaboration.

Sincerely,

**ANITA G. DAVID, EdD**
SUC President IV
